

## Lab 2: Agile Backlog Creation & Sprint Simulation in Jira


Municipal Infrastructure Damage Reporting App


Name-Sahajpreet Singh

SRN-PES1UG24CS397


### Epics & User Stories / Backlog

All three Epics were created in Jira, broken down from the Lab 1 functional requirements. The progress bars below show completion status after running two sprints.

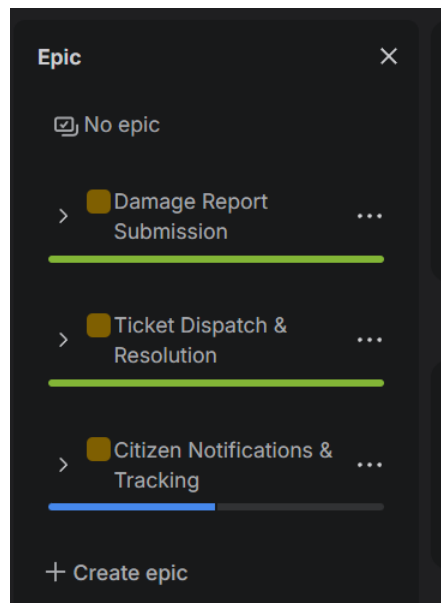

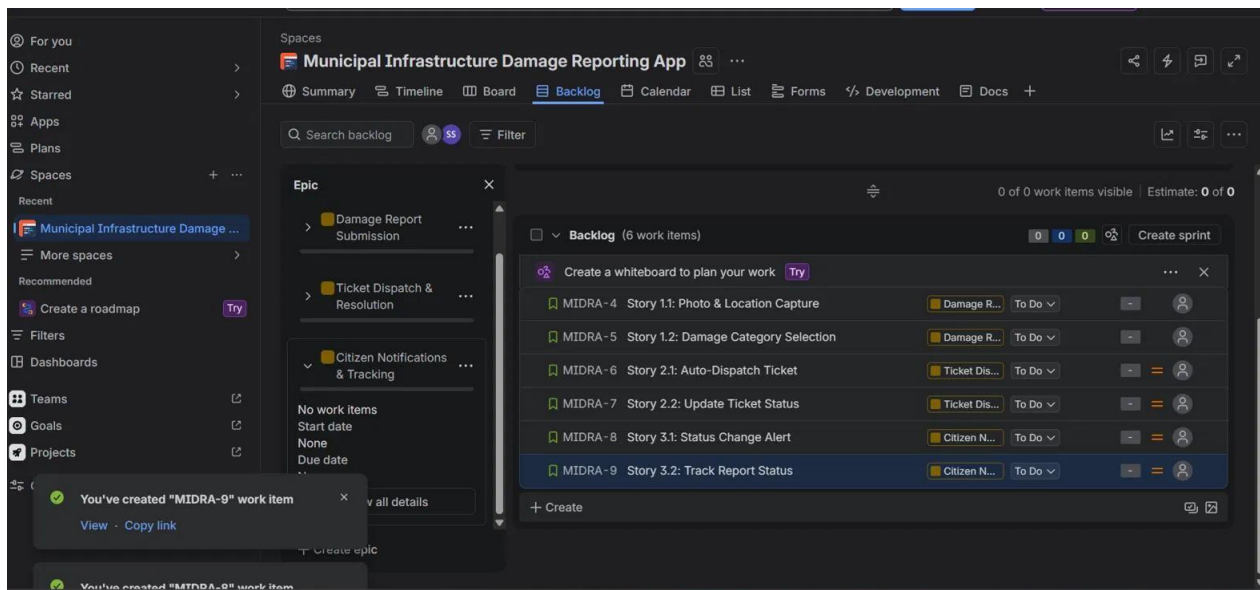

## Story Points

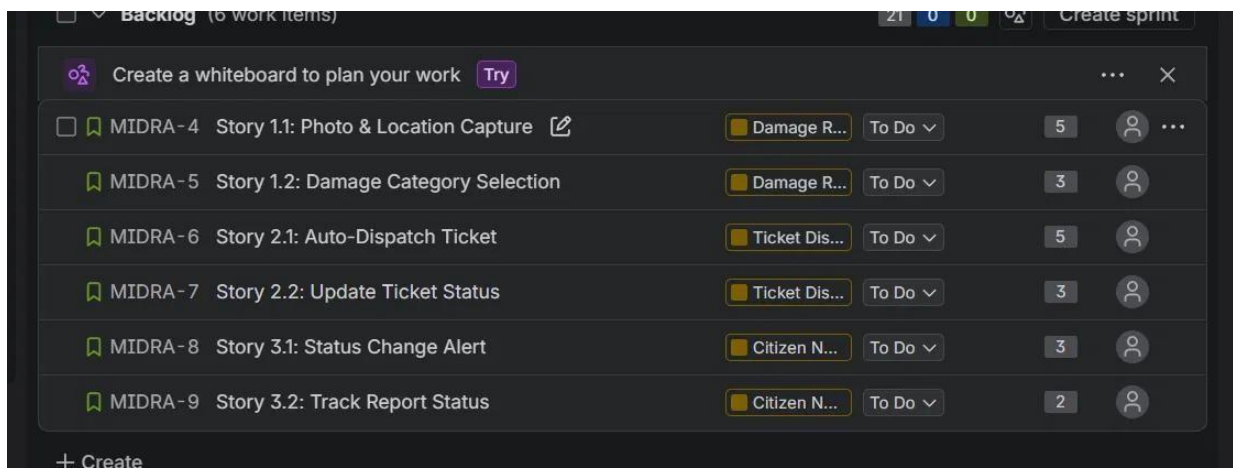

## Active Sprint Board

The screenshot displays a Kanban-style sprint board with a dark theme. The top navigation bar includes links for Summary, Timeline, Board (selected), Backlog, Calendar, List, Forms, Development, and Docs. Below the navigation bar, there is a search bar, a user profile icon, a filter button, and a group button. A 'Complete sprint' button is located in the top right corner.

The board is divided into three columns:

- To Do (1 item):** Contains 'Story 2.1: Auto-Dispatch Ticket'. The parent is 'Ticket Dispatch & Resolution'. It is assigned to 'MIDRA-6' with a priority of 5.
- In Progress (0 items):** Currently empty, with a '+ Create' button.
- Done (2 items):** Contains 'Story 1.2: Damage Category Selection' and 'Story 1.1: Photo & Location Capture'. Both have a parent of 'Damage Report Submission'. Story 1.2 is assigned to 'MIDRA-5' with a priority of 3 and a checkmark. Story 1.1 is assigned to 'MIDRA-4' with a priority of 5 and a checkmark.

Each item card includes a '+ Create' button at the bottom.



Backlog insights



Use these insights to plan your next sprint.

Sprint: MIDRA Sprint 3

Sprint commitment



Previous sprint



MIDRA Sprint 2

| Completed | Committed | Total complete |
|-----------|-----------|----------------|
| 8 points  | 13 points | 61%            |

Work type breakdown




Your top work item type to focus on in this sprint.




# Burndown Chart

## Sprint 1

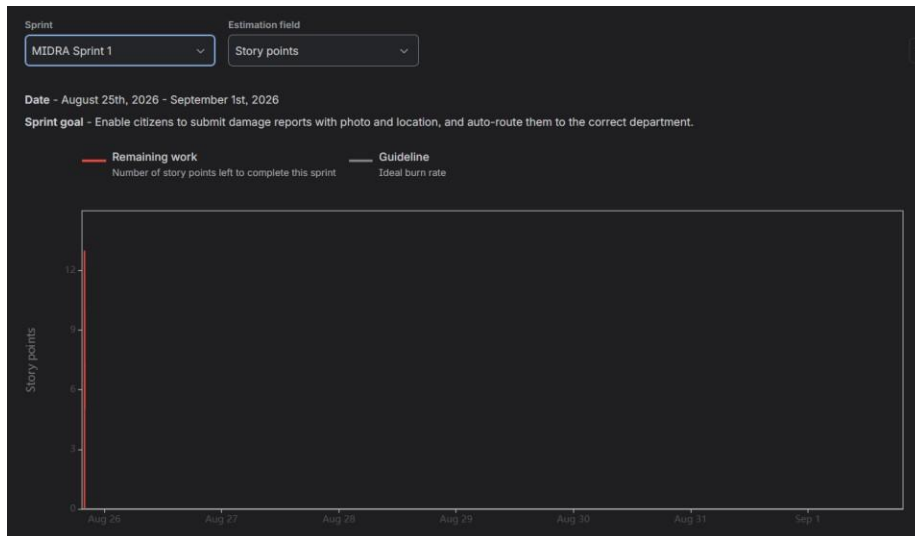

## Sprint 2

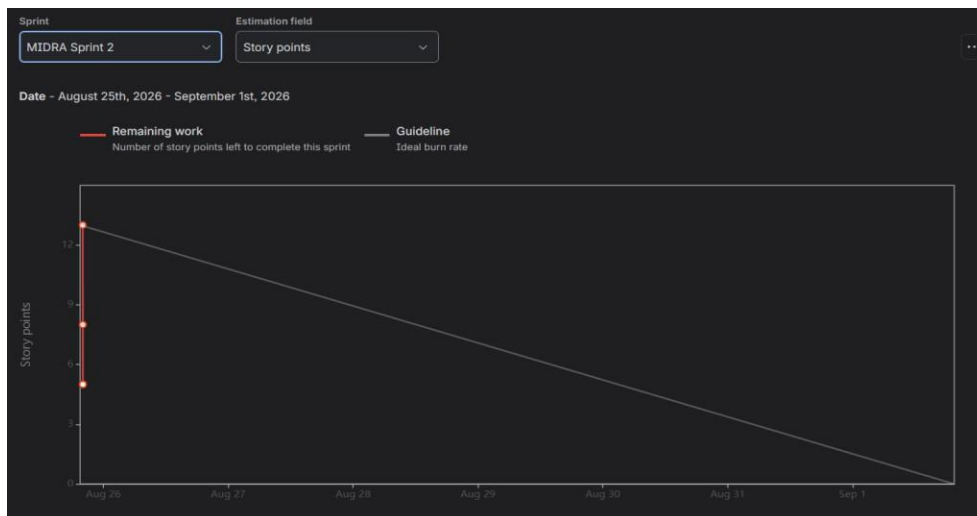

## **Reflection answers**

### **1. Did your estimations reflect the actual effort?**

Not entirely. Story points were assigned using the Fibonacci scale (5, 3, 5, 3, 3, 2) based on perceived complexity, but since this was a simulated sprint rather than real development, all “work” was marked complete almost instantly instead of over the planned one-week window. In a real team setting, these estimates would need to be validated against actual time spent on each story and adjusted in future sprints.

### **2. Was your backlog well-prioritized?**

Yes. Epic 1 (Damage Report Submission) was prioritized first because photo capture, GPS extraction, and category selection are prerequisites for everything downstream. Epic 2 (Ticket Dispatch & Resolution) followed, since it depends on a report already existing, and Epic 3 (Citizen Notifications & Tracking) was scheduled last, as notifications only make sense once tickets can change status.

### **3. How did your simulated sprint align with your plan?**

Sprint 1 completed 2 of 3 planned stories (8 of 13 points), with Story 2.1: Auto-Dispatch Ticket left incomplete and rolled into Sprint 2. Sprint 2 then completed 2 of 4 stories (8 of 13 points), leaving Story 3.2: Track Report Status unfinished. This reflects a realistic pattern where foundational stories (report submission) are finished on schedule while later, dependency-heavy stories (dispatch, tracking) slip behind.

### **4. What insights did the burndown chart give about your team's capacity?**

In Sprint 1, the remaining-work line dropped to zero almost immediately, well ahead of the guideline — a sign that the sprint may have been under-scoped for the time box, or that the team could take on more work per sprint. In Sprint 2, the line dropped partway (13 to 5 points) and then plateaued below where the guideline predicted, showing that roughly half the committed work stalled while the rest finished early — suggesting uneven task sizing rather than a steady, predictable burn rate.

## **Jira Project/Workspace link**

[https://sahaj78.atlassian.net/jira/software/projects/MIDRA/boards/34?filter=textfields+%7E+%22SP\\*%22&groupBy=none&atlOrigin=eyJpIjoZTY3YjU1M2Y0M2IzNGJiNTg1OTRhMzcwNTYyZmMxMDQiLCJwIjoiaj9](https://sahaj78.atlassian.net/jira/software/projects/MIDRA/boards/34?filter=textfields+%7E+%22SP*%22&groupBy=none&atlOrigin=eyJpIjoZTY3YjU1M2Y0M2IzNGJiNTg1OTRhMzcwNTYyZmMxMDQiLCJwIjoiaj9)
